


ID	Task Name	Duration	Mar 3, '13							Mar 10, '13							Mar 17, '13						
			T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W
1	<b>Scenario Planning</b>	40 days																					
2	Establish a Vision	15 days																					
3	Establish a Process	15 days																					
4	Develop Scenarios	10 days																					
5	<b>Requirements Analysis</b>	30 days																					
6	Define Information Content and Context	15 days																					
7	Build Domain Model	15 days																					
8	<b>Mapping and Modeling</b>	30 days																					
9	Mapping	15 days																					
10	Define Terms with Exchange Partner	15 days																					
11	<b>Building and Validating</b>	60 days																					
12	Identify Reference Schemas	10 days																					
13	Create Subset Schema	5 days																					
14	Create Extension Schema	15 days																					
15	Create Exchange Schema	10 days																					
16	Build Constraint Schema	10 days																					
17	Validate Schema	10 days																					
18	<b>Assemble and Document</b>	20 days																					
19	Develop Meta-Data Schema	10 days																					
20	Assemble Required IEPD Artifacts	10 days																					
21	<b>Publish IEPD</b>	10 days																					
22	Publish IEPD to Repository	10 days																					
23	<b>Data Exchange Design Implementation</b>	65 days																					
24	Design Instance Creation Rules (Sender)	10 days																					
25	Design Instance Processing Rules (Receiver)	10 days																					
26	Design Instance middleware routing rules based on data exchange	10 days																					
27	Document Business Use Cases for data exchange	10 days																					
28	Document Business Test Cases for data exchange	15 days																					
29	MOU's for Data Exchange and Network Services	10 days																					
30	<b>Data Exchange Development and Implementation</b>	30 days																					
31	Develop Instance and Implement Creation Rules	15 days																					
32	Develop Instance receiver and related system processing rules	10 days																					
33	Develop middleware data exchange business process and routing rules based on the business case	5 days																					

Project: Person Data Exchange Projec  
Date: Tue 7/7/15


Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			



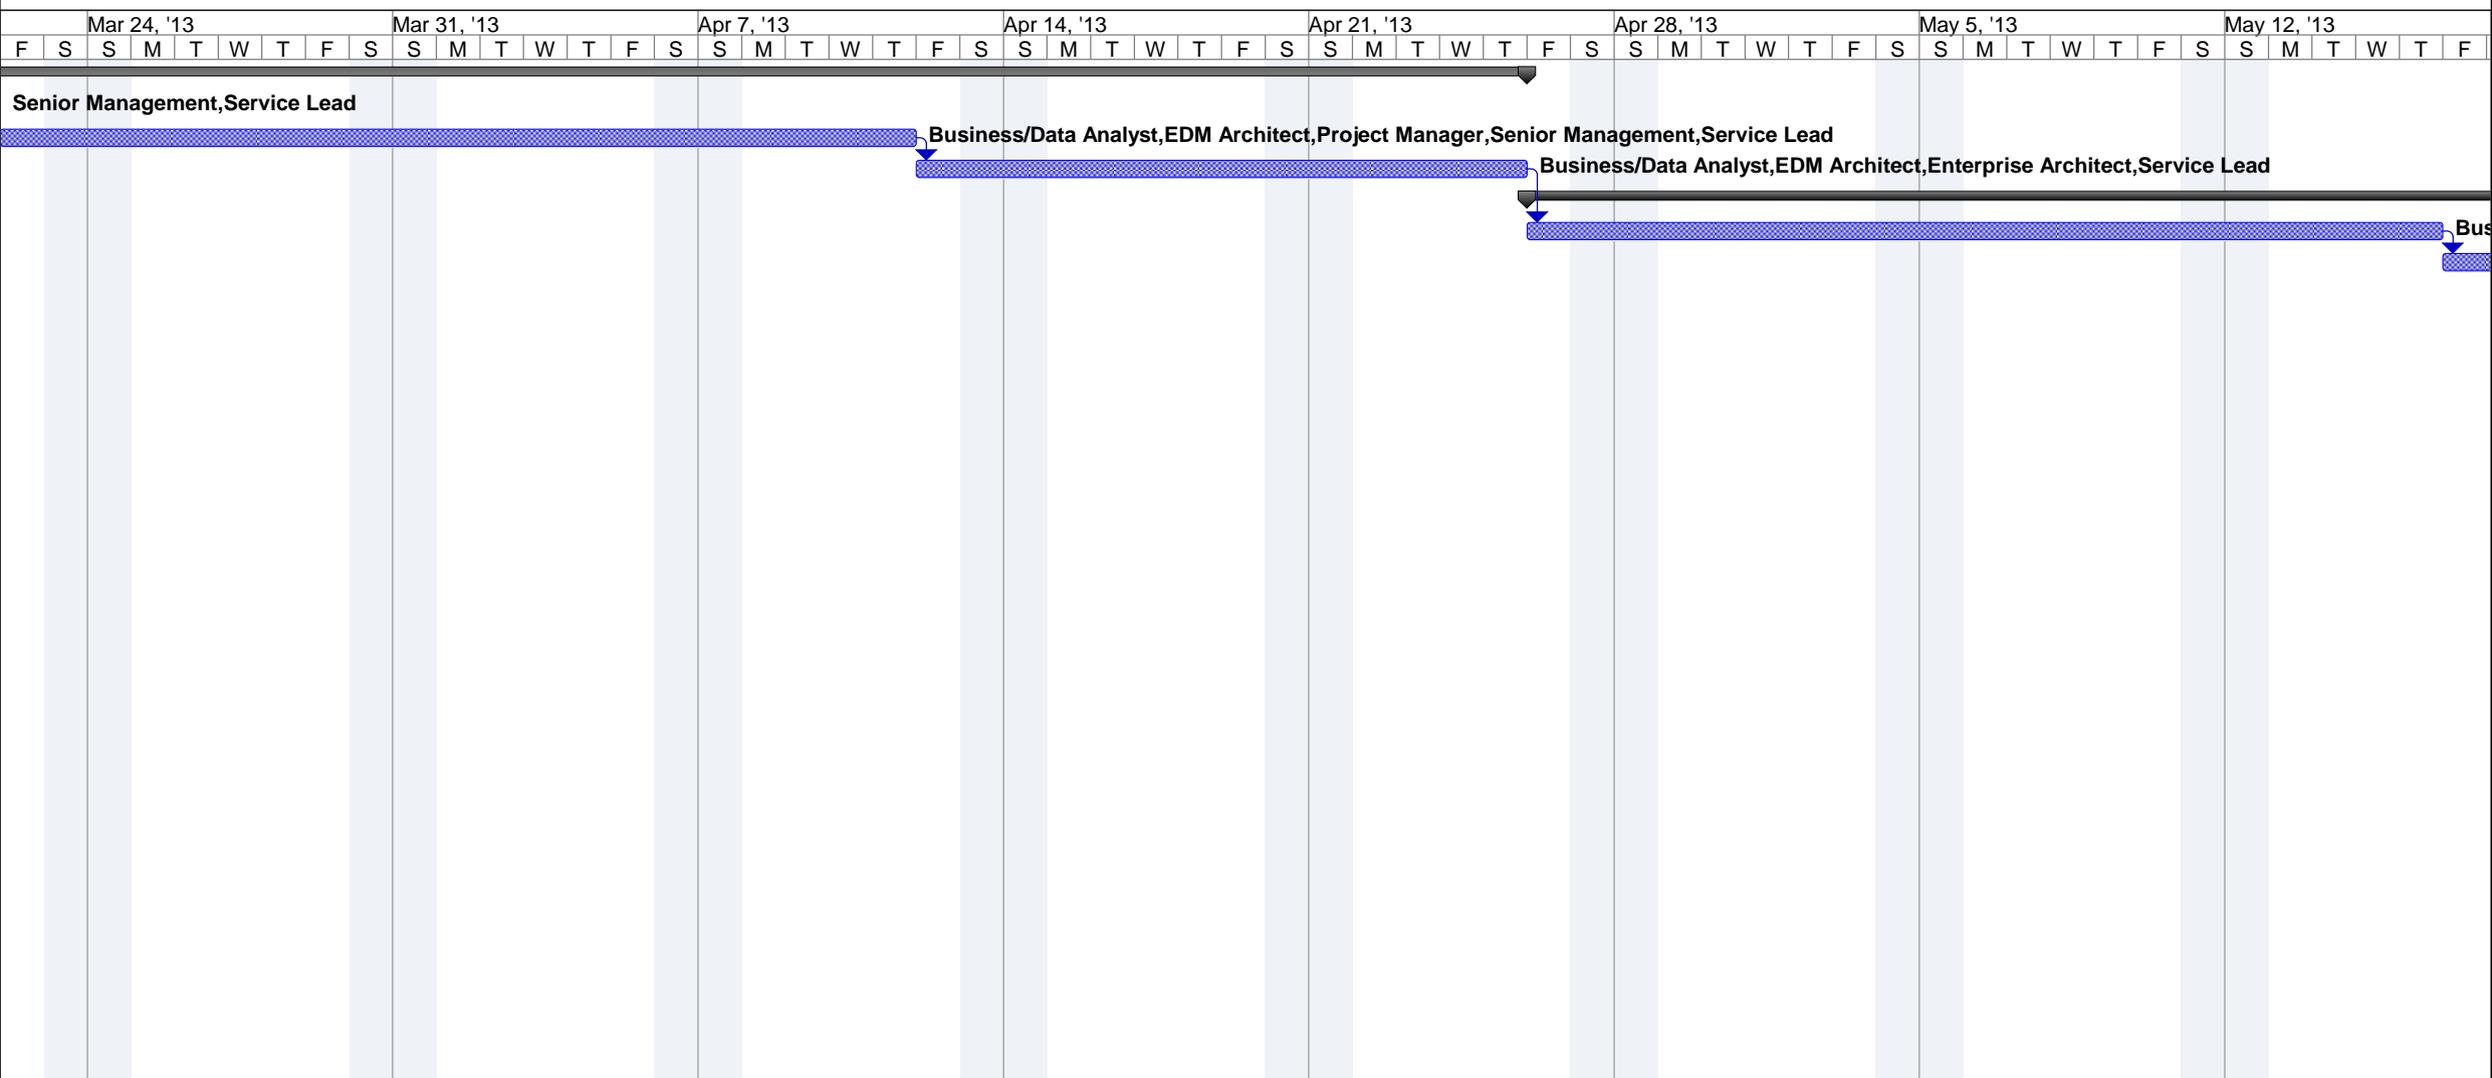


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

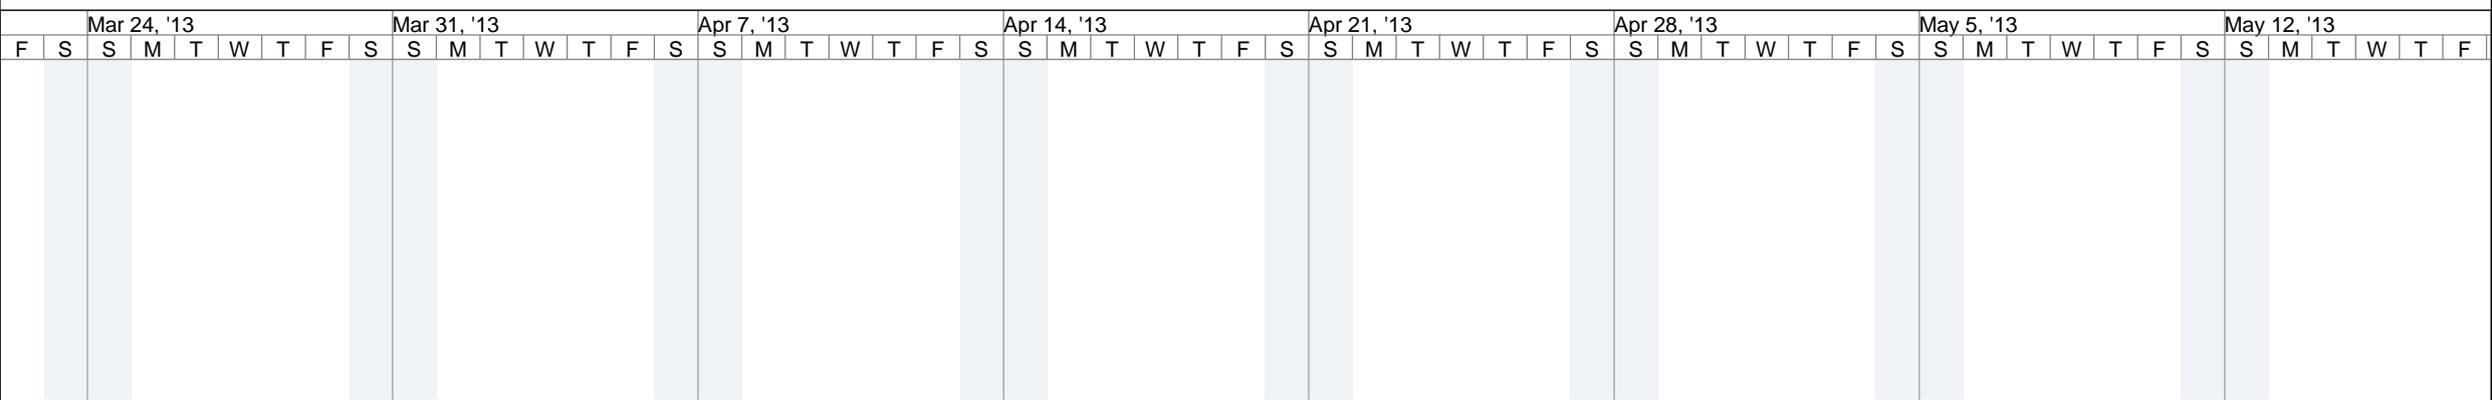

Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

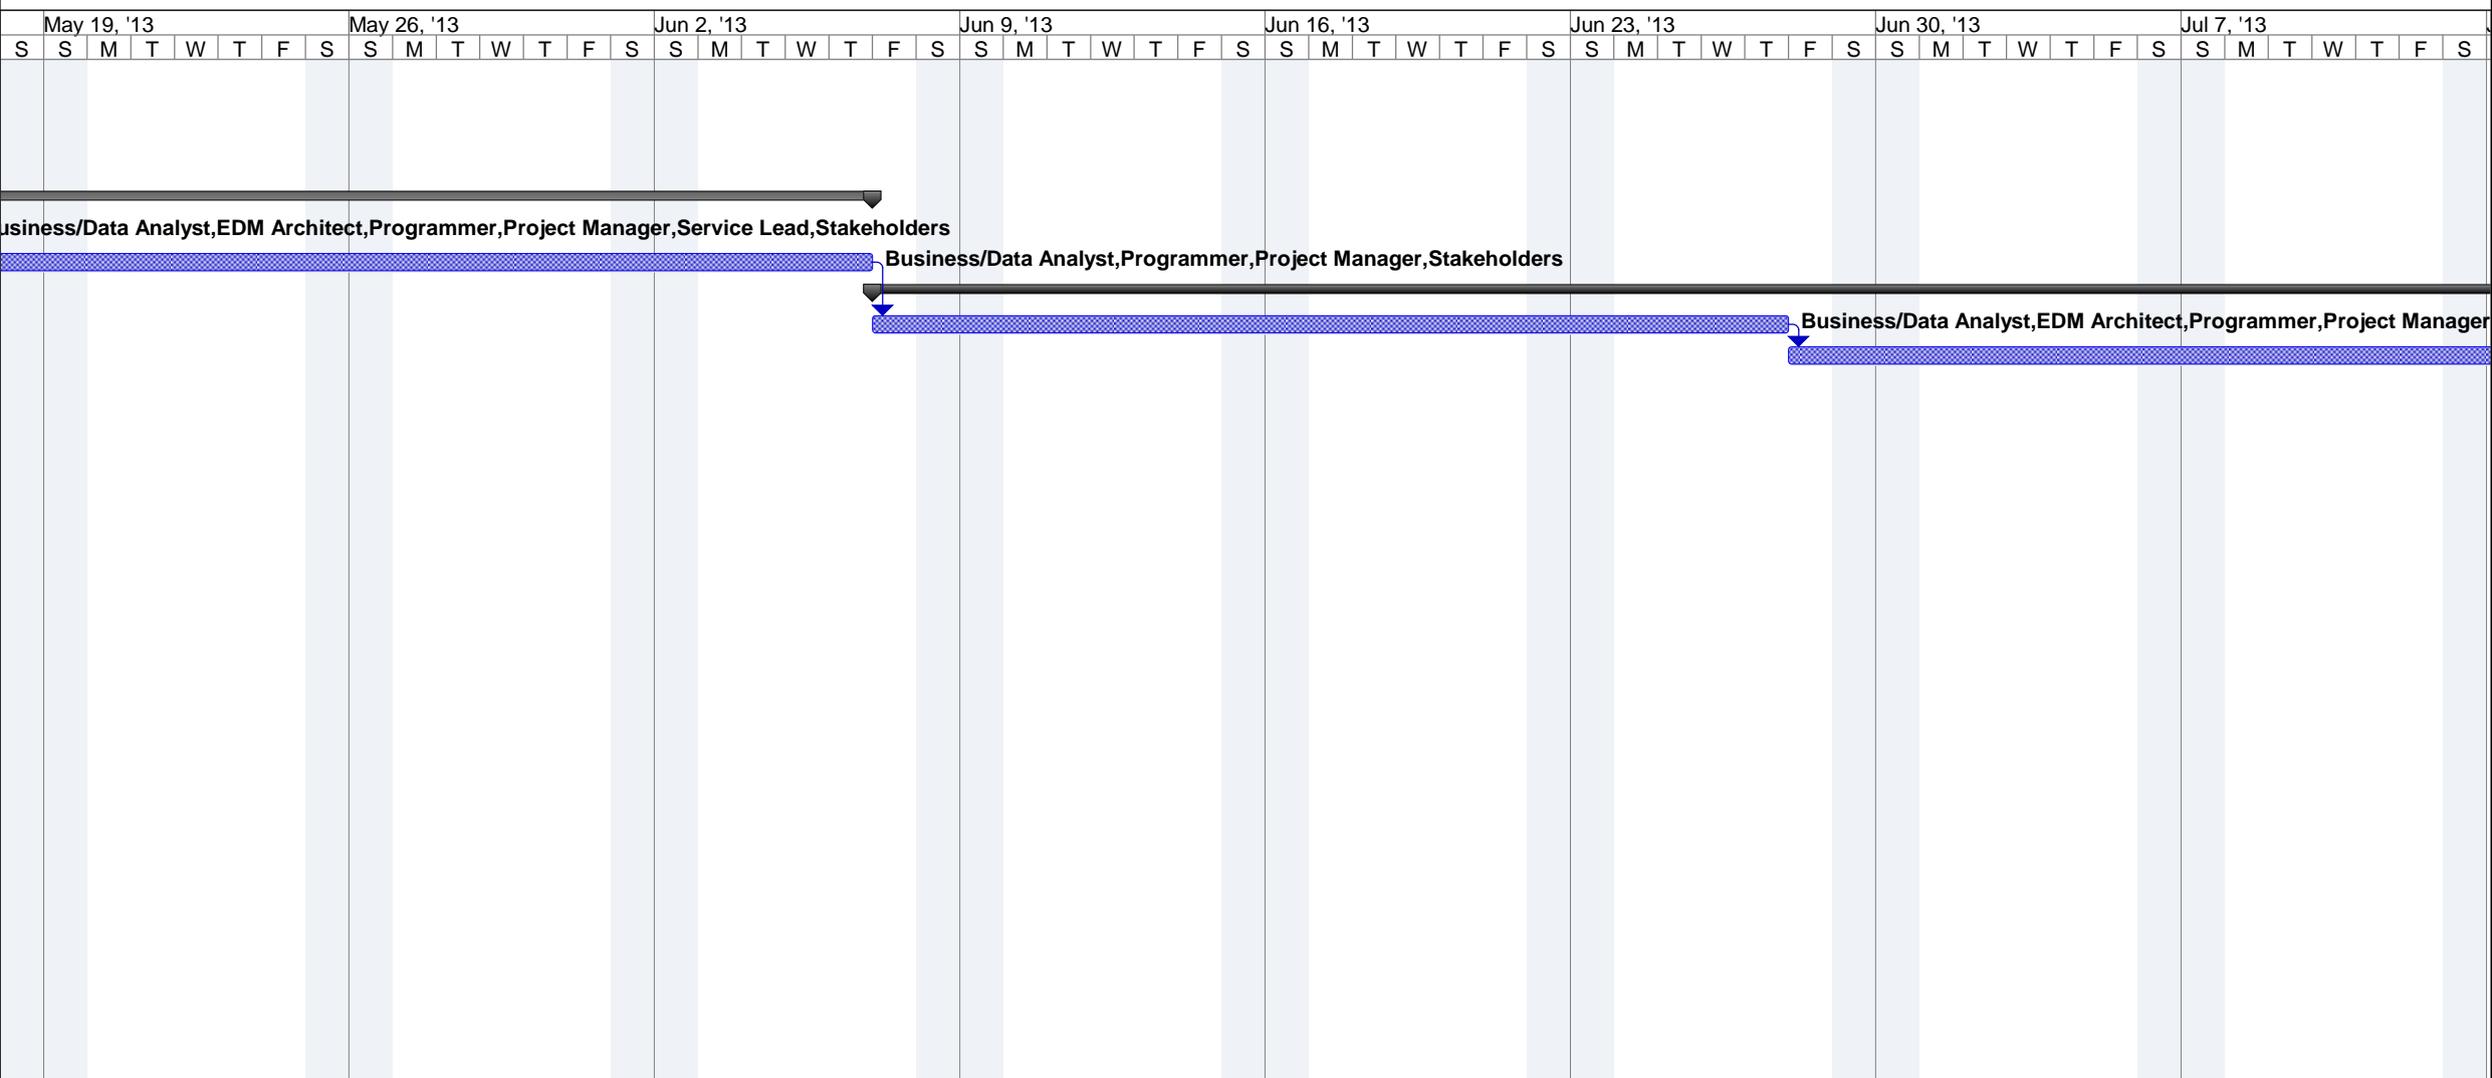


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

May 19, '13							May 26, '13							Jun 2, '13							Jun 9, '13							Jun 16, '13							Jun 23, '13							Jun 30, '13							Jul 7, '13														
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							


Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

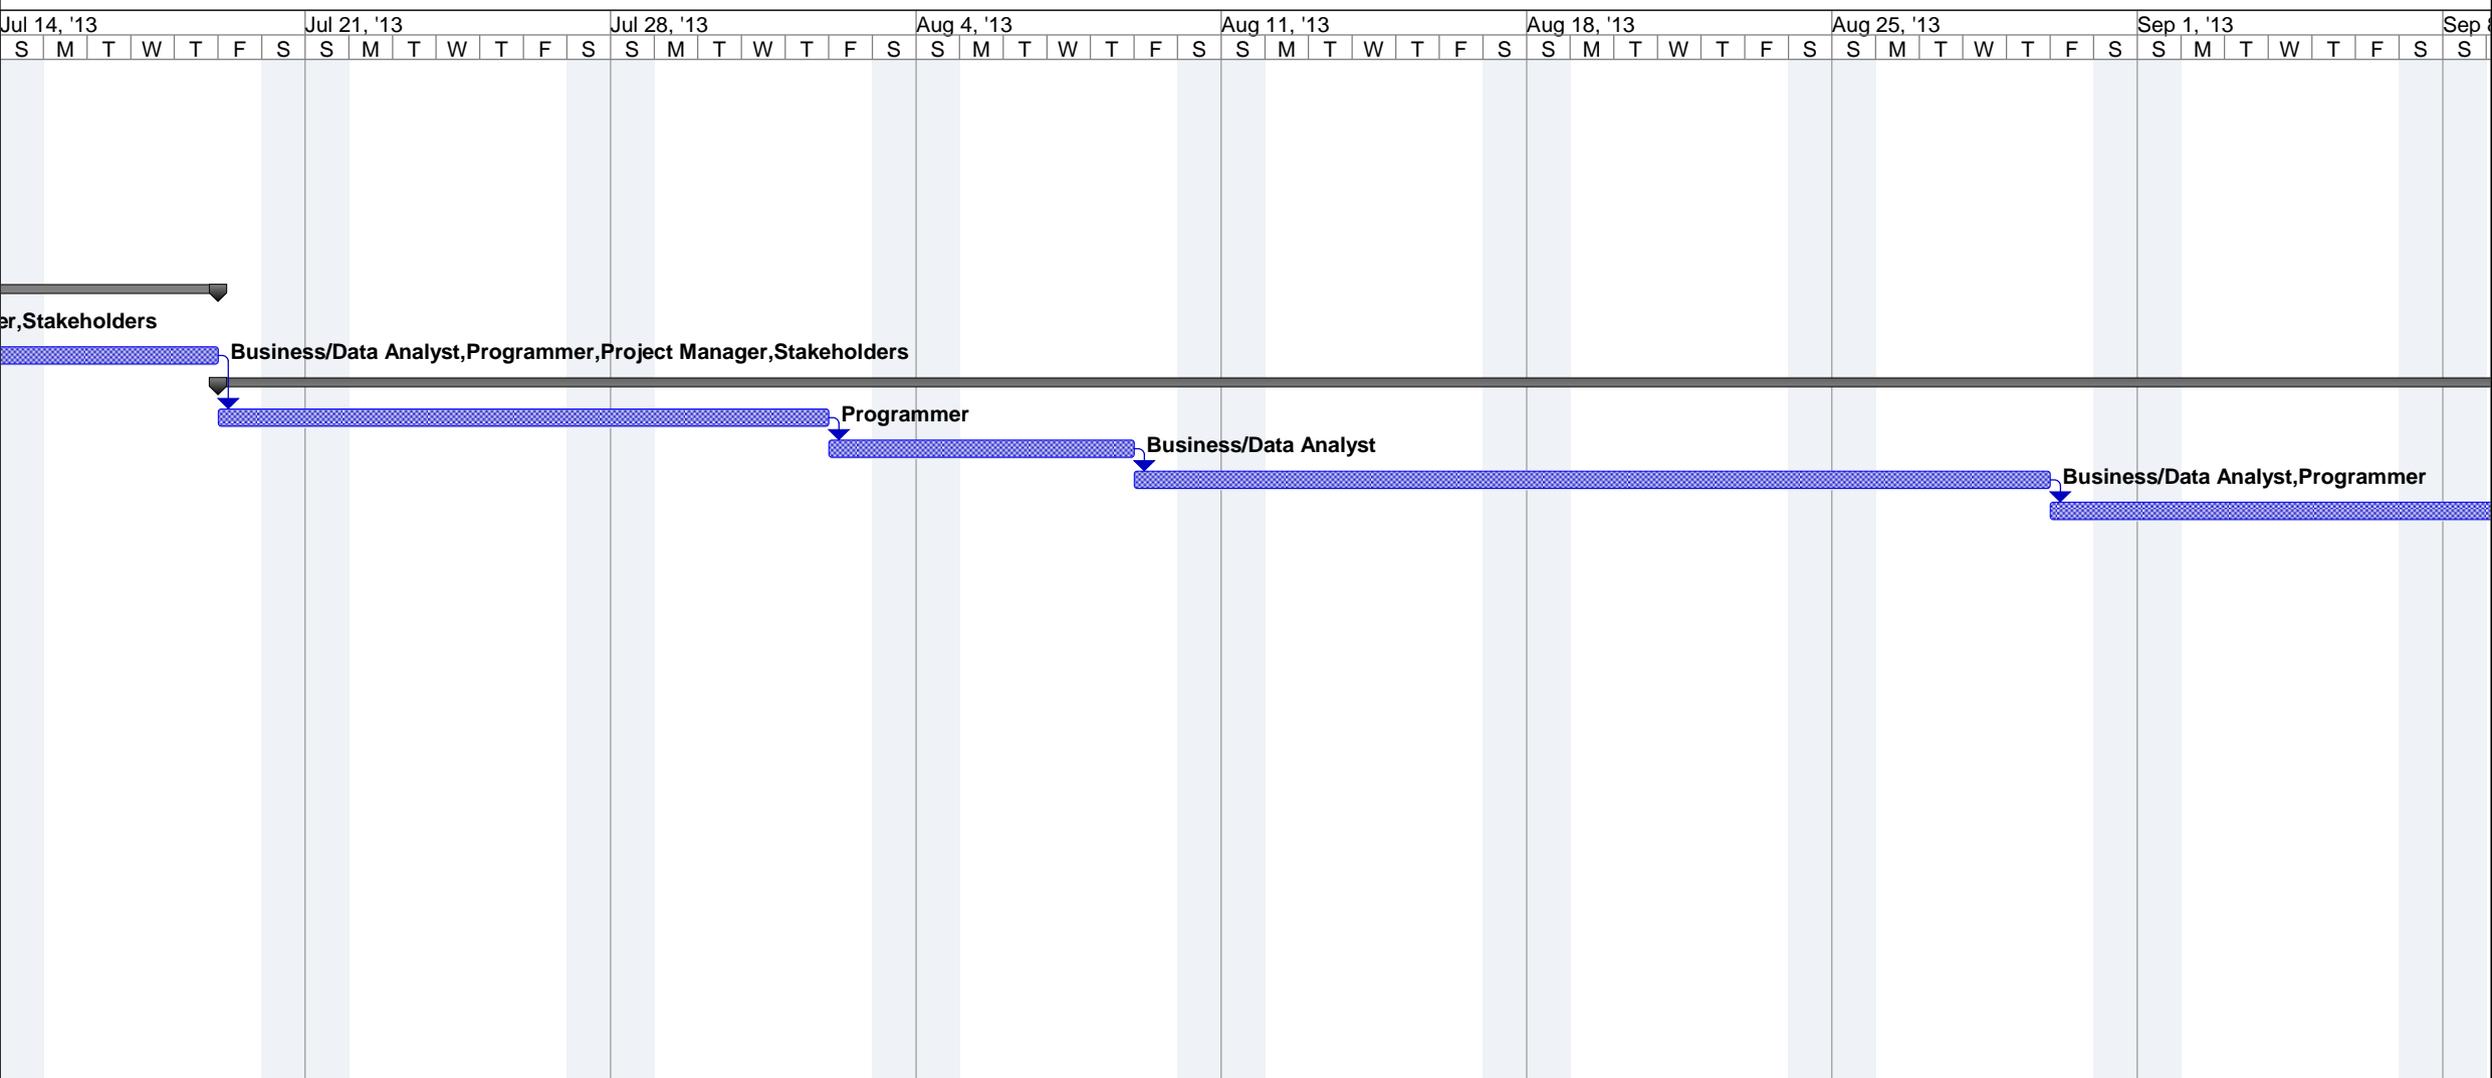


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

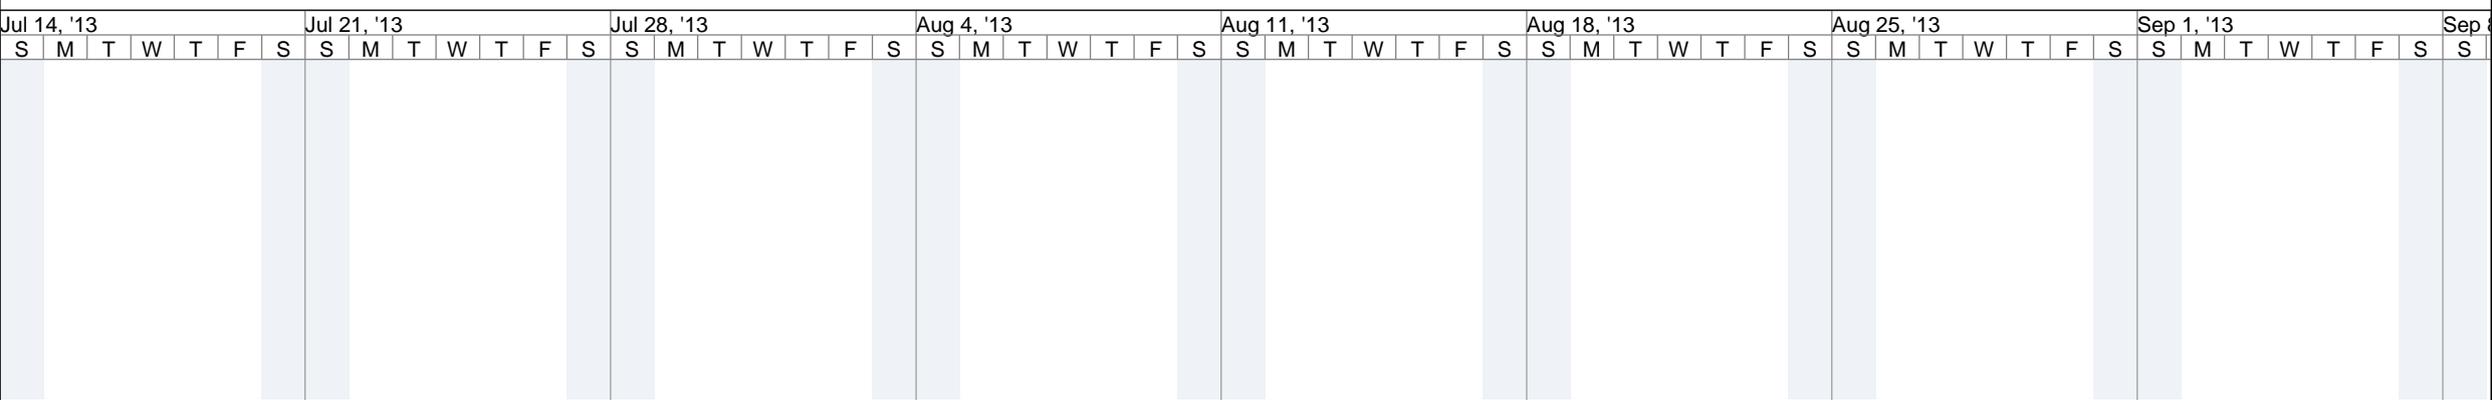


Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

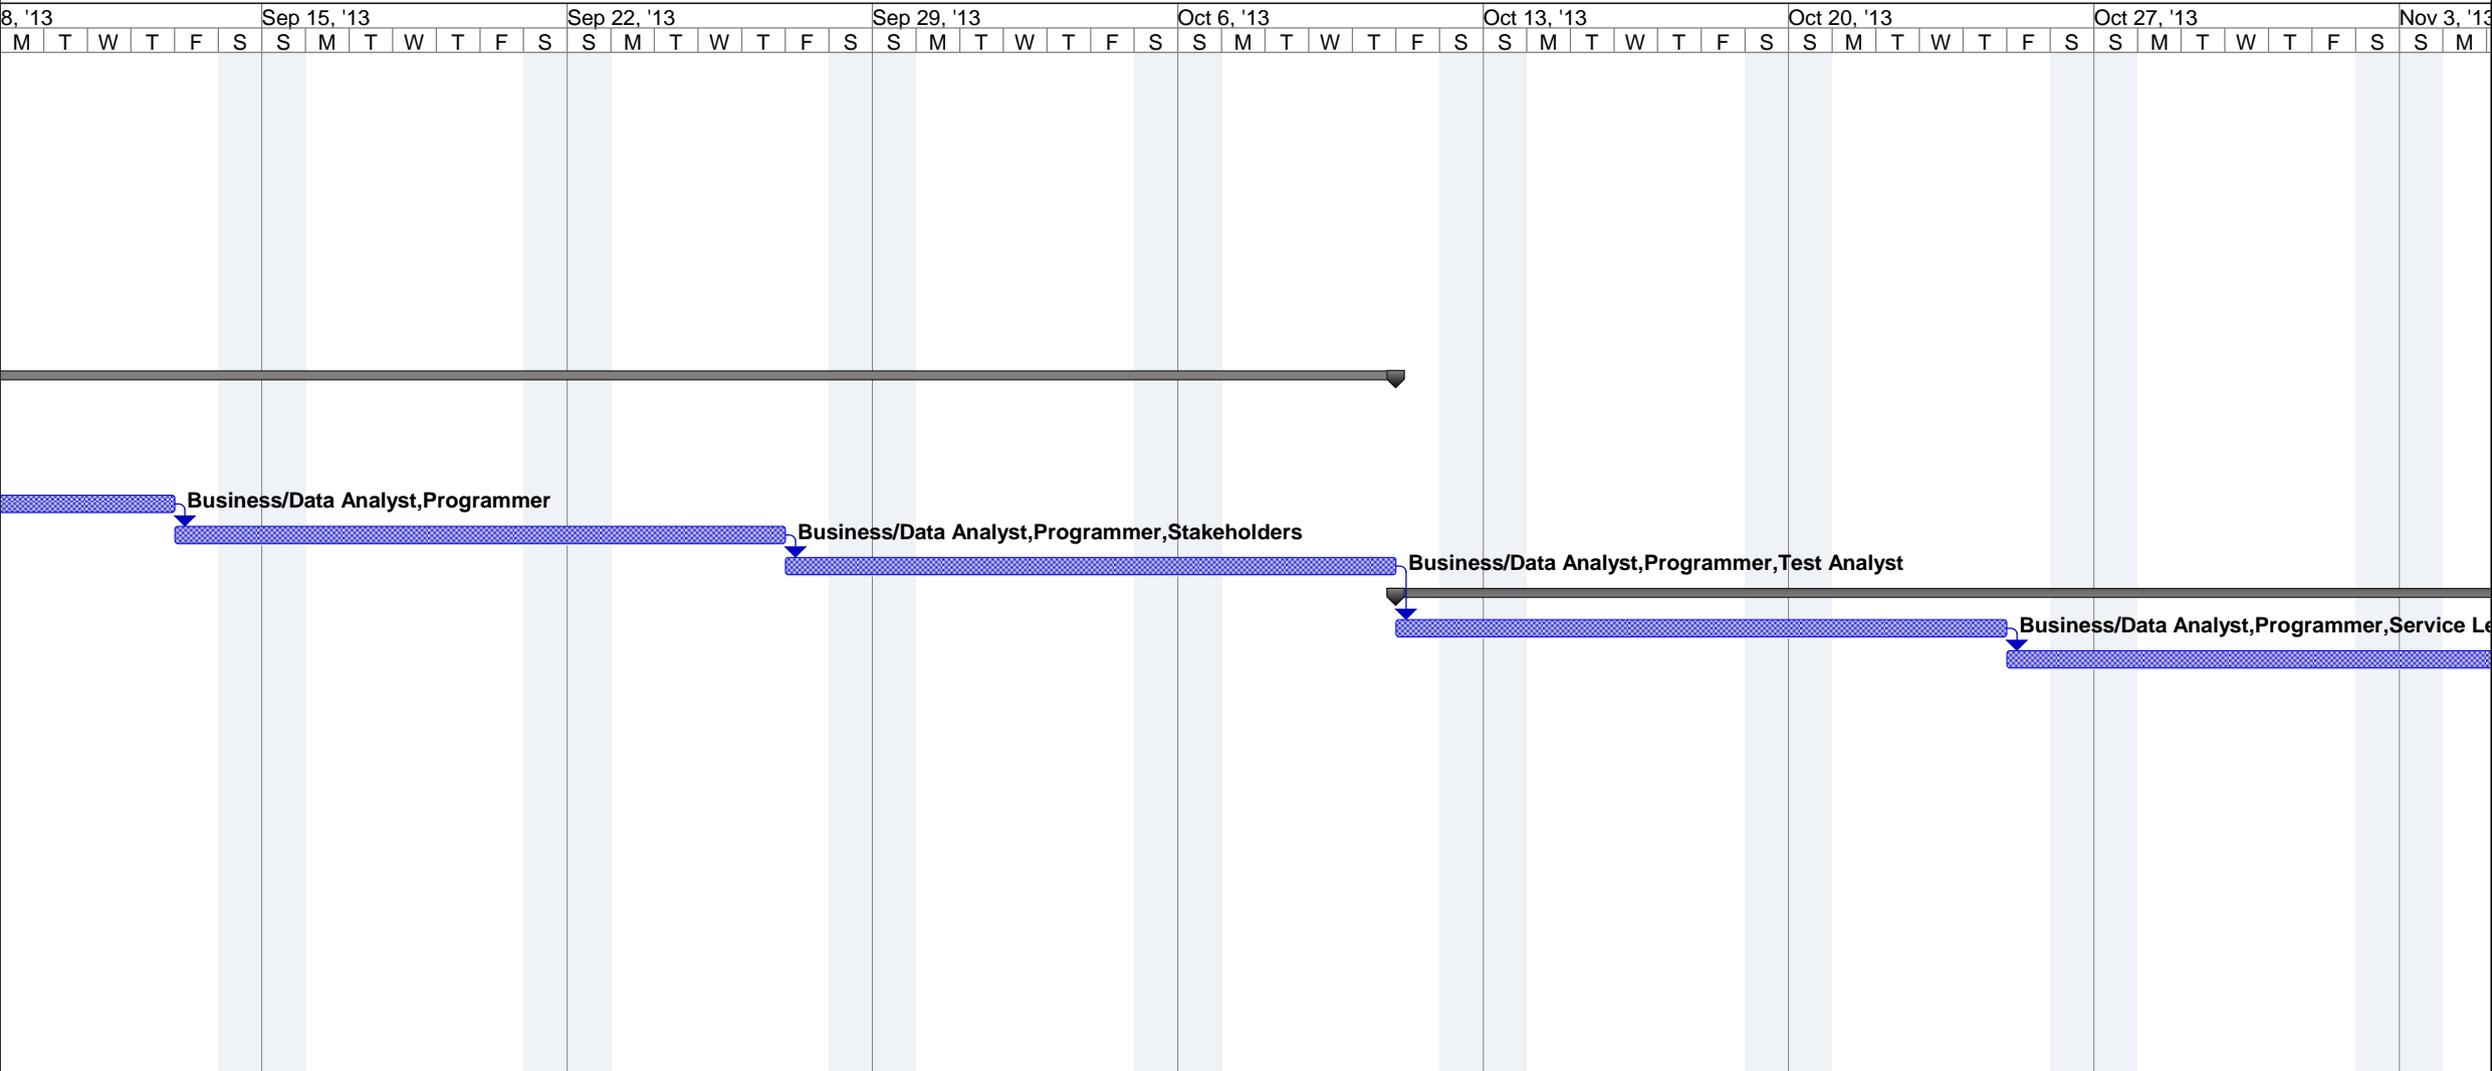


Project: Person Data Exchange Projec  
Date: Tue 7/7/15




Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

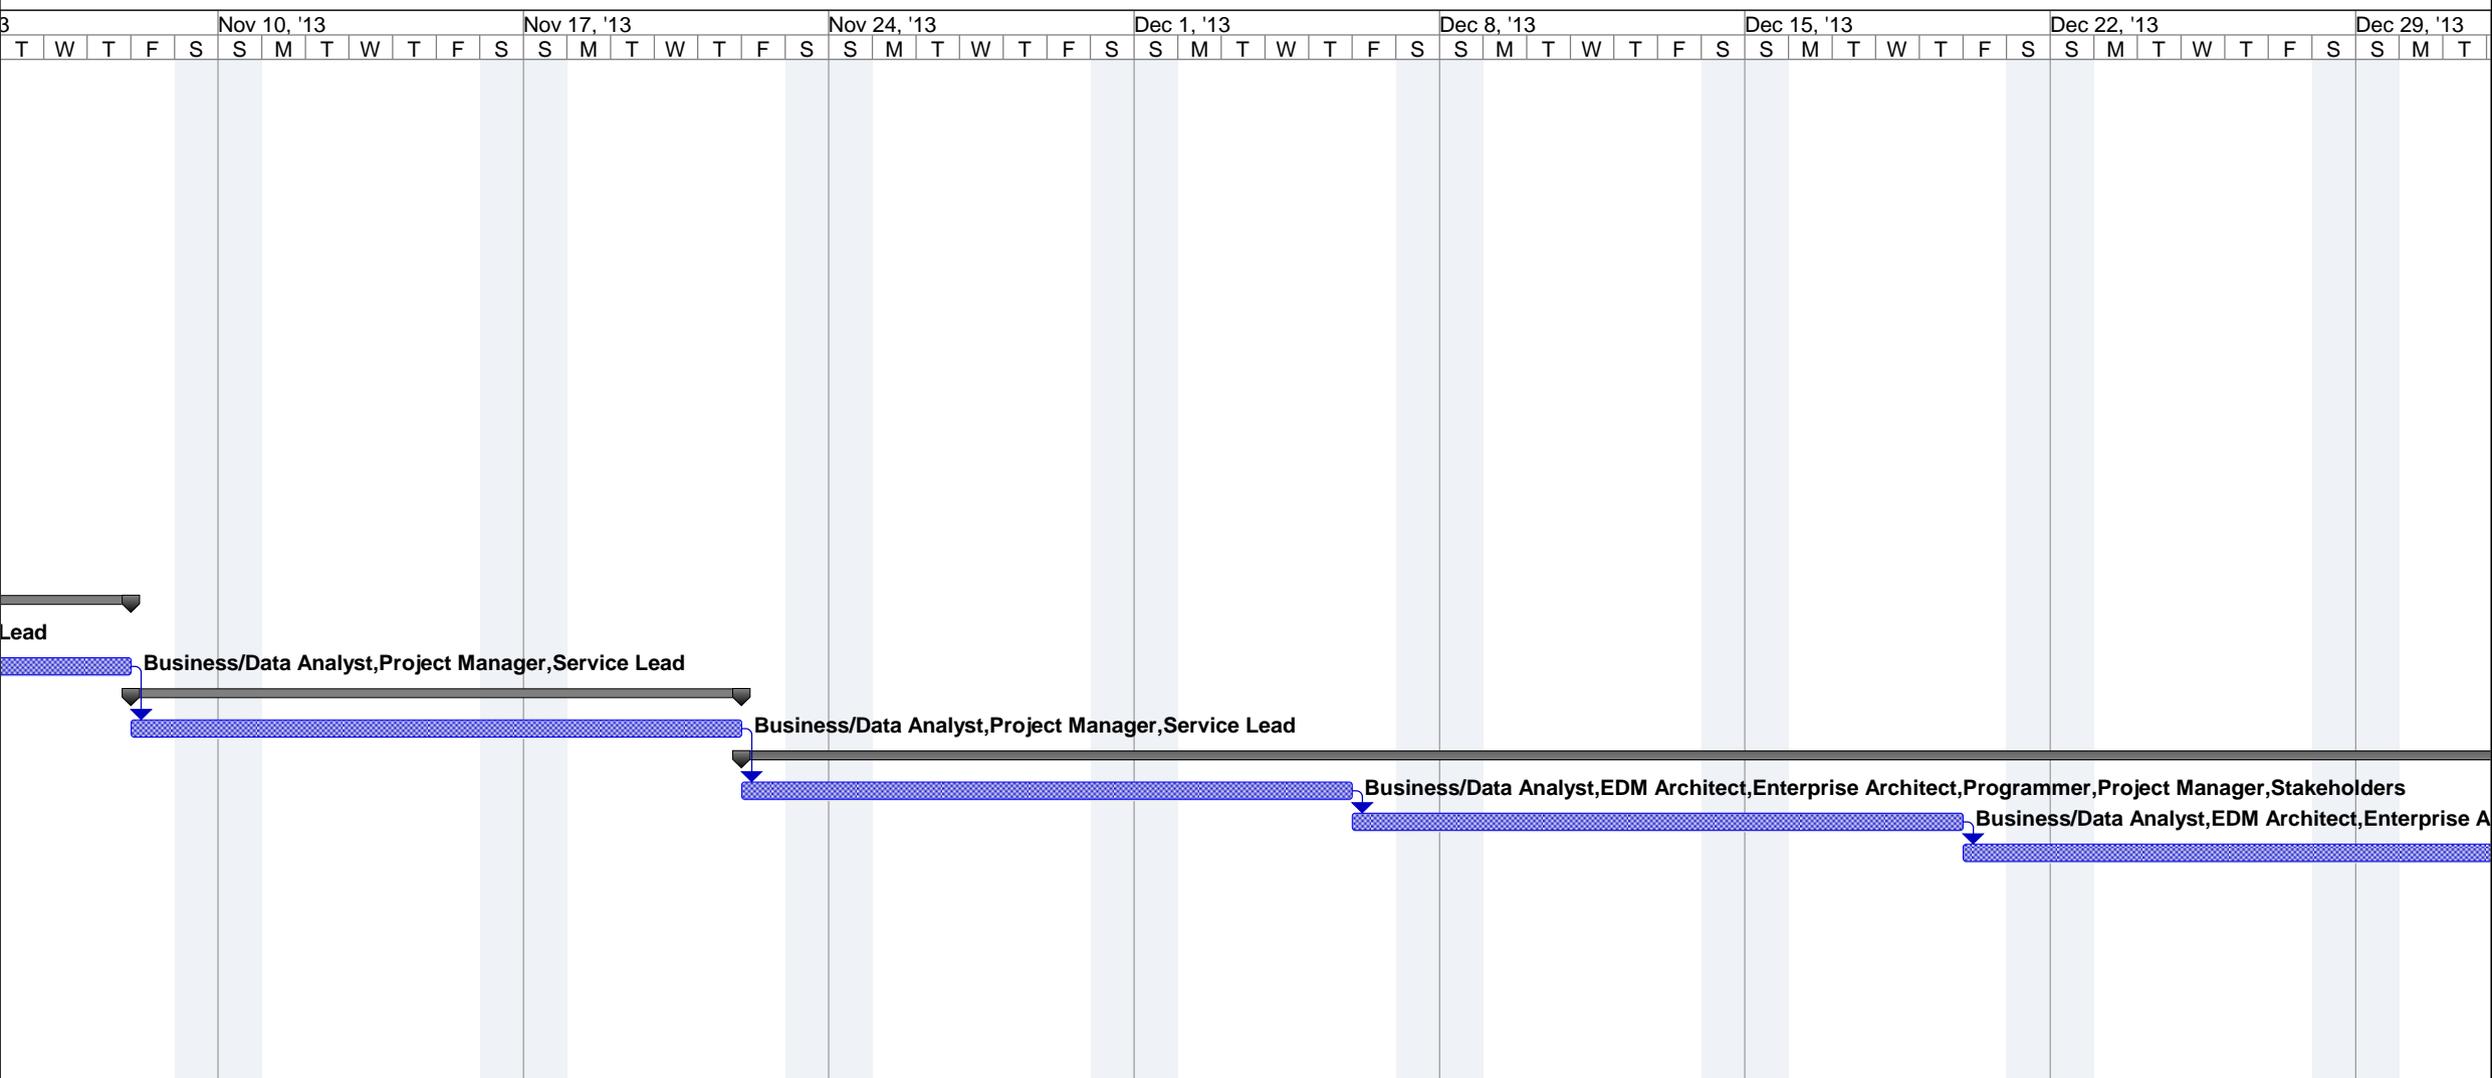


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			




Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

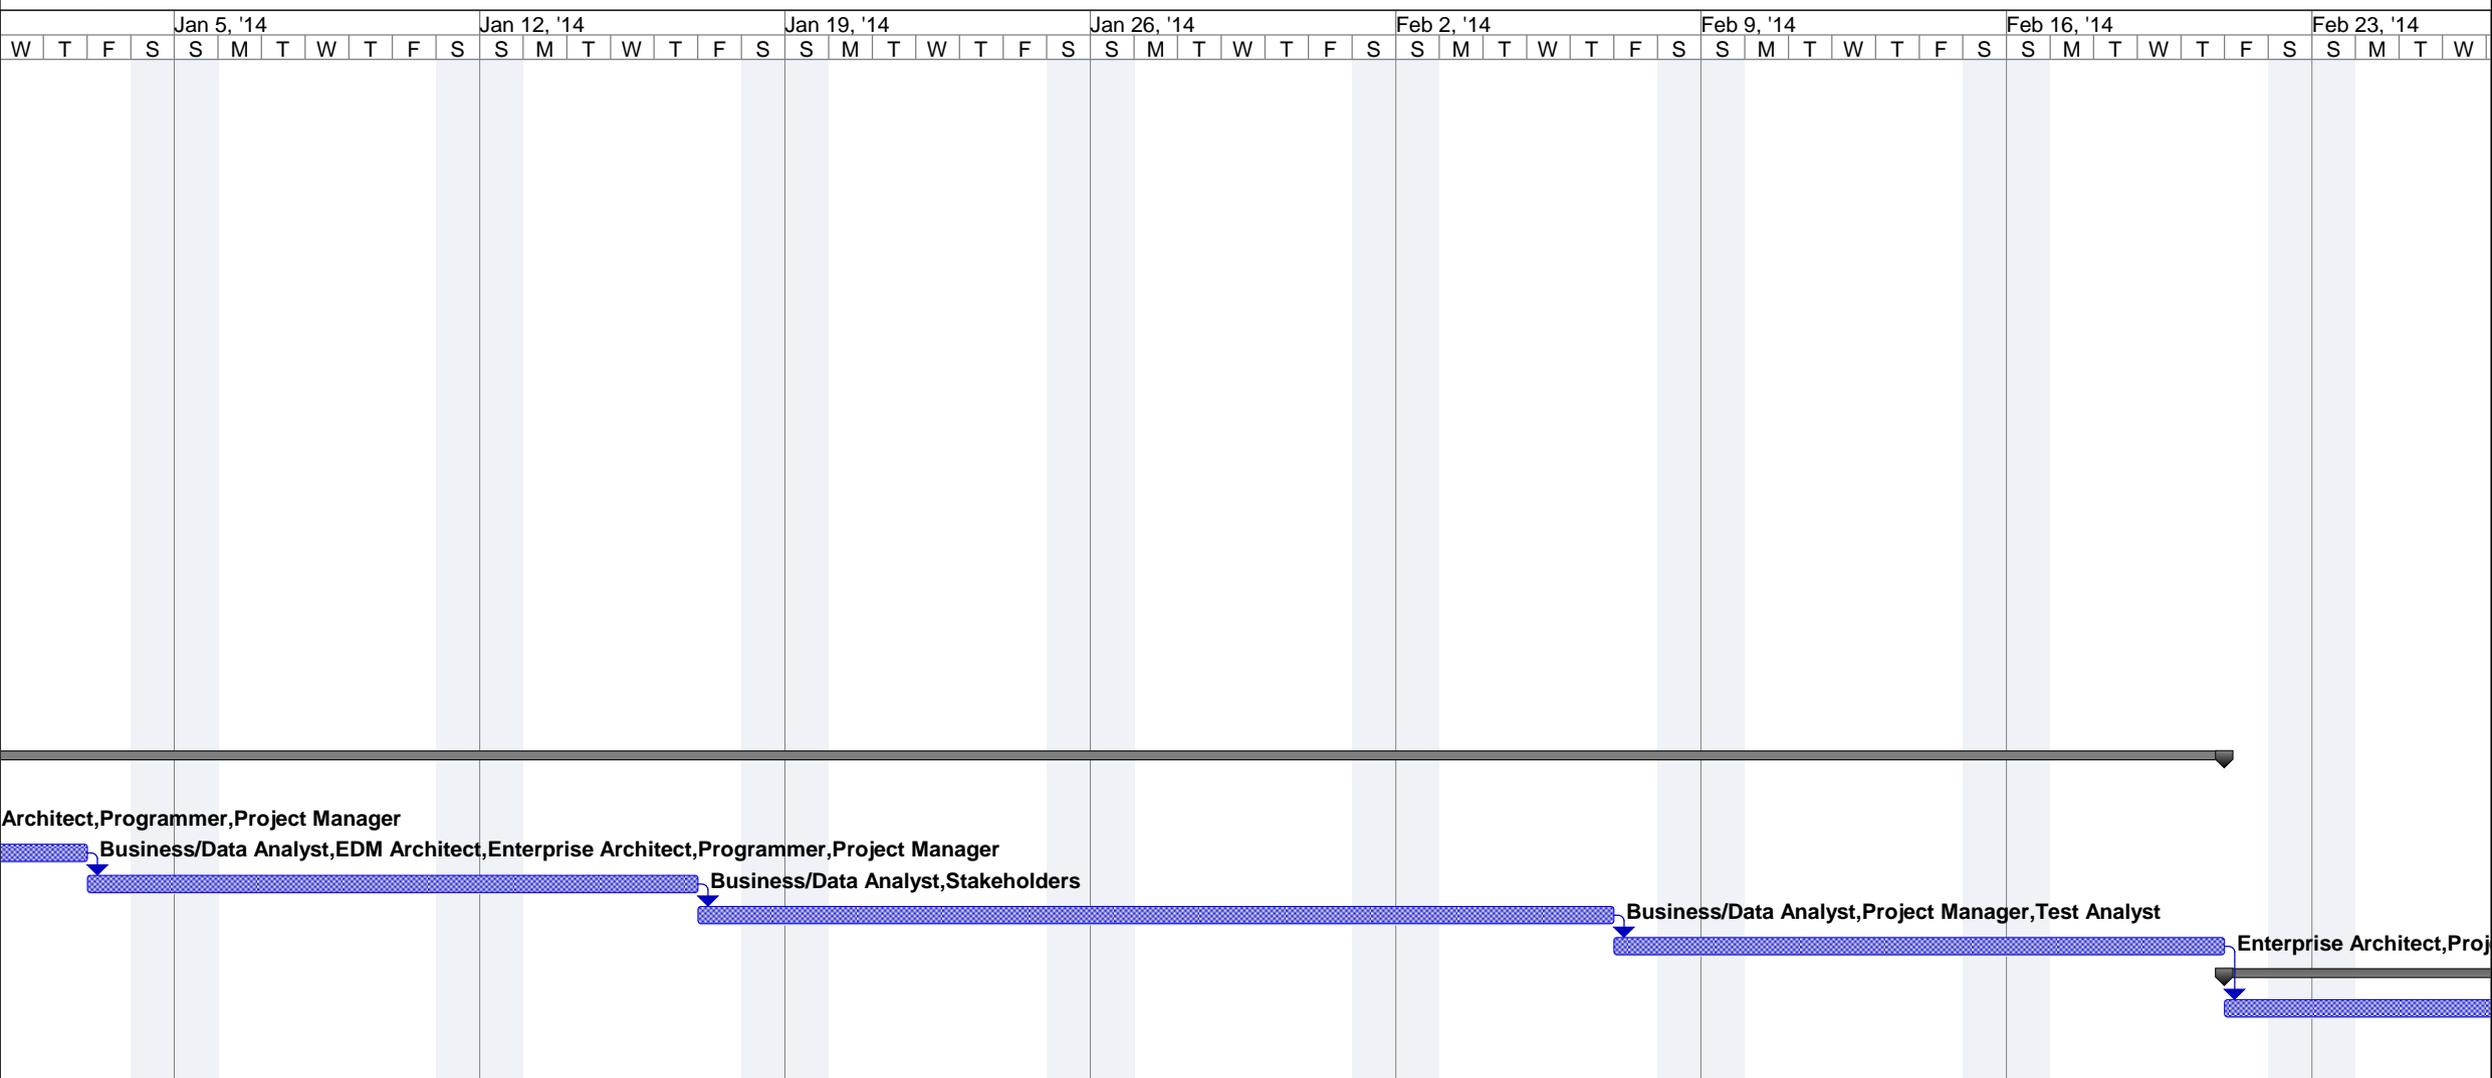


Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			




Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

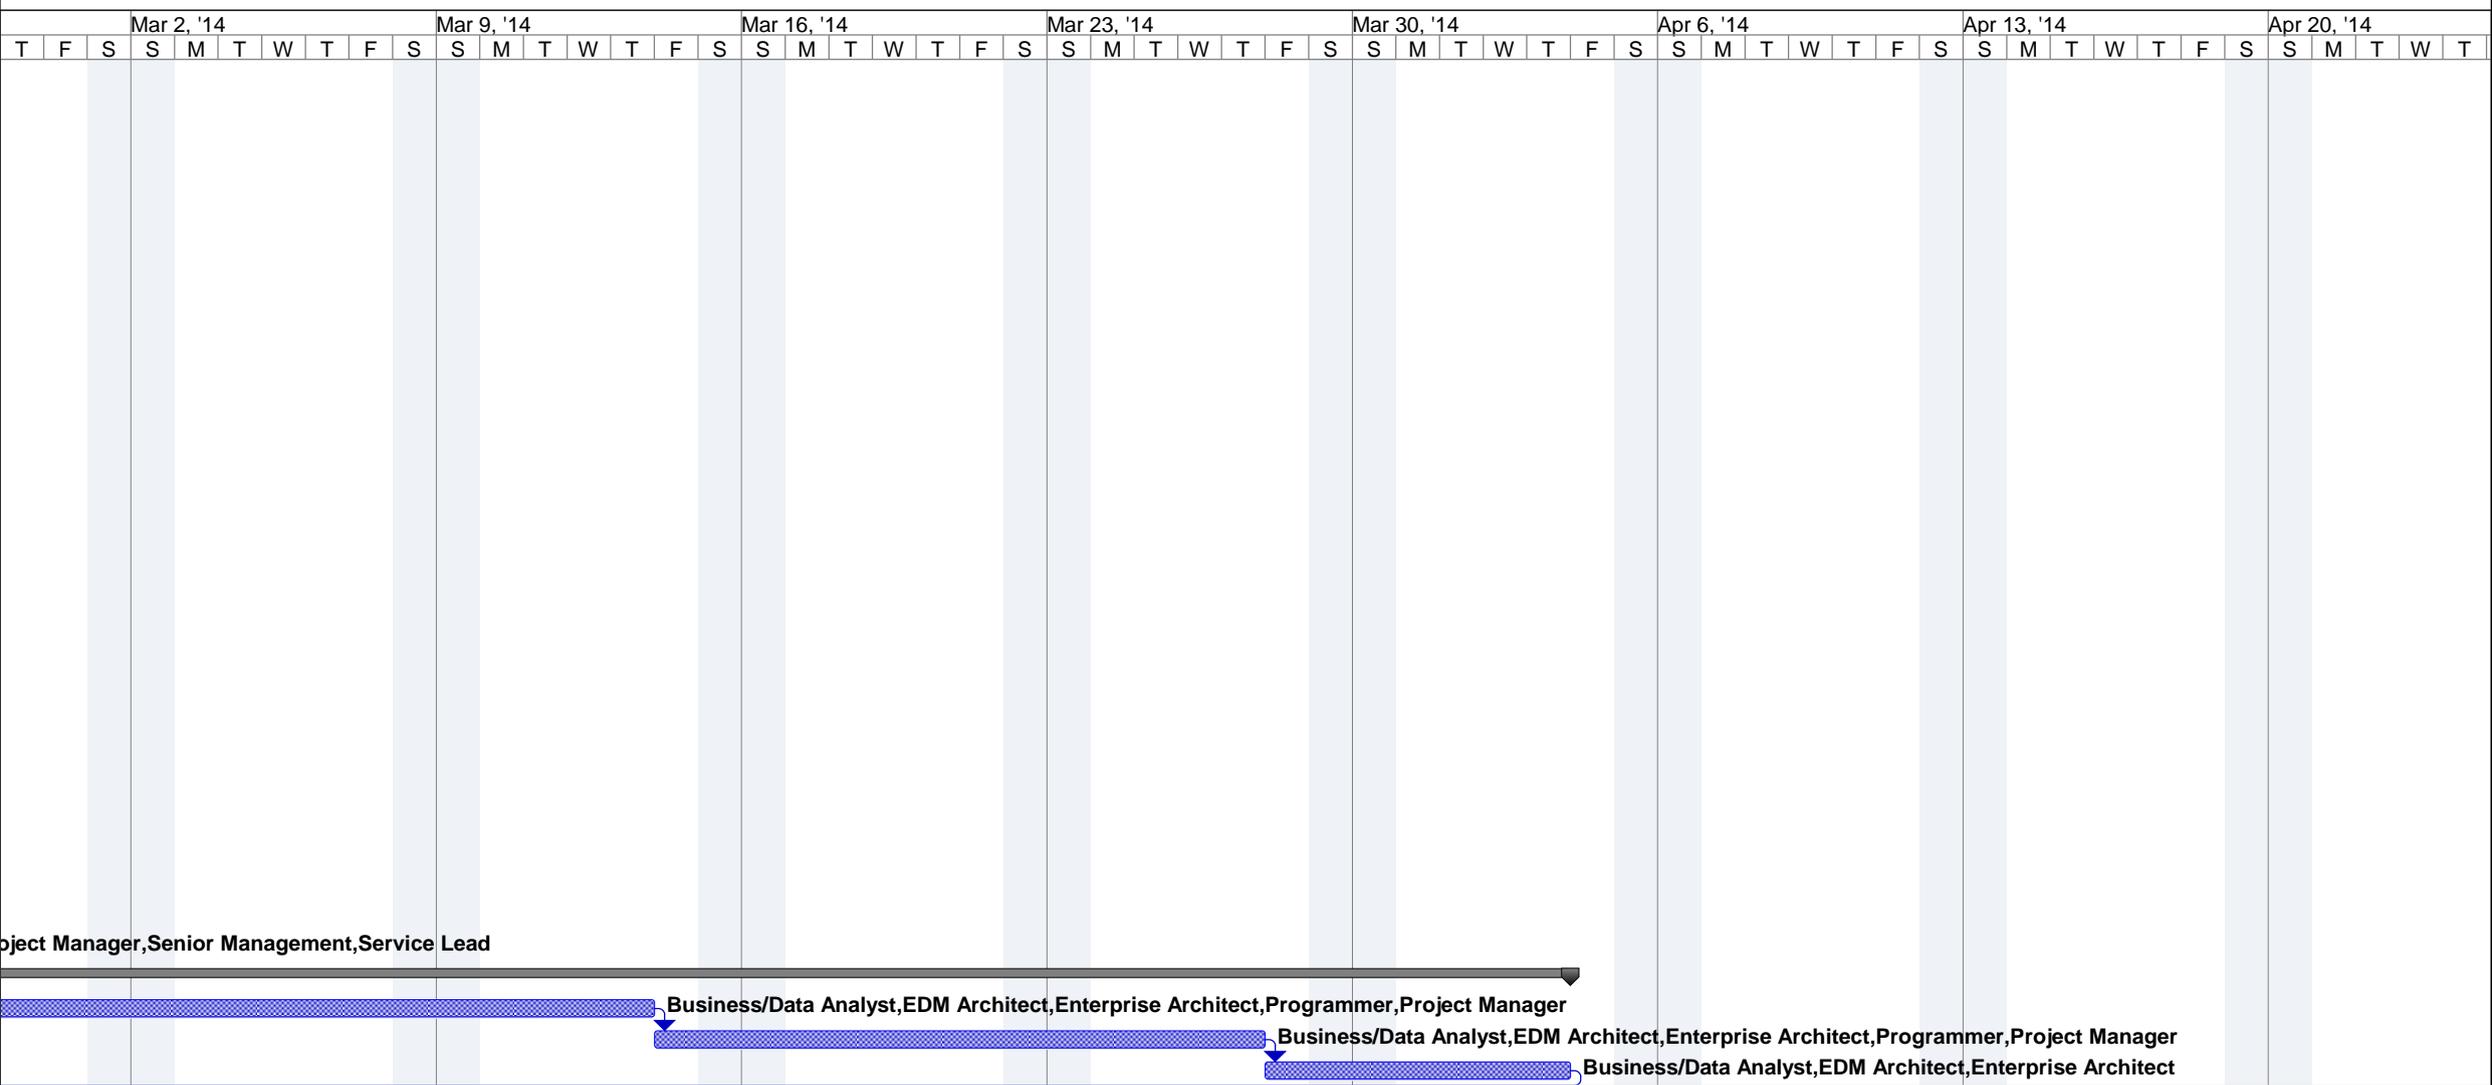


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

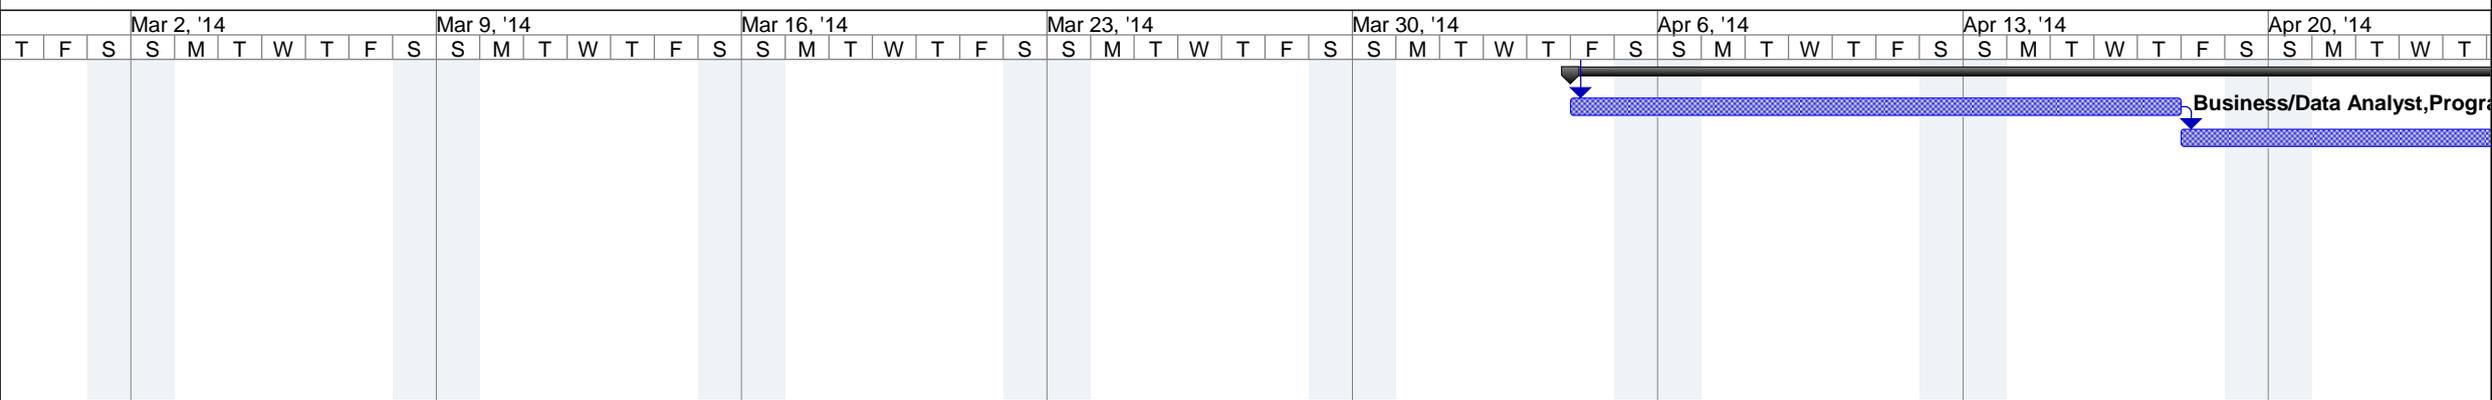


Project: Person Data Exchange Projec  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

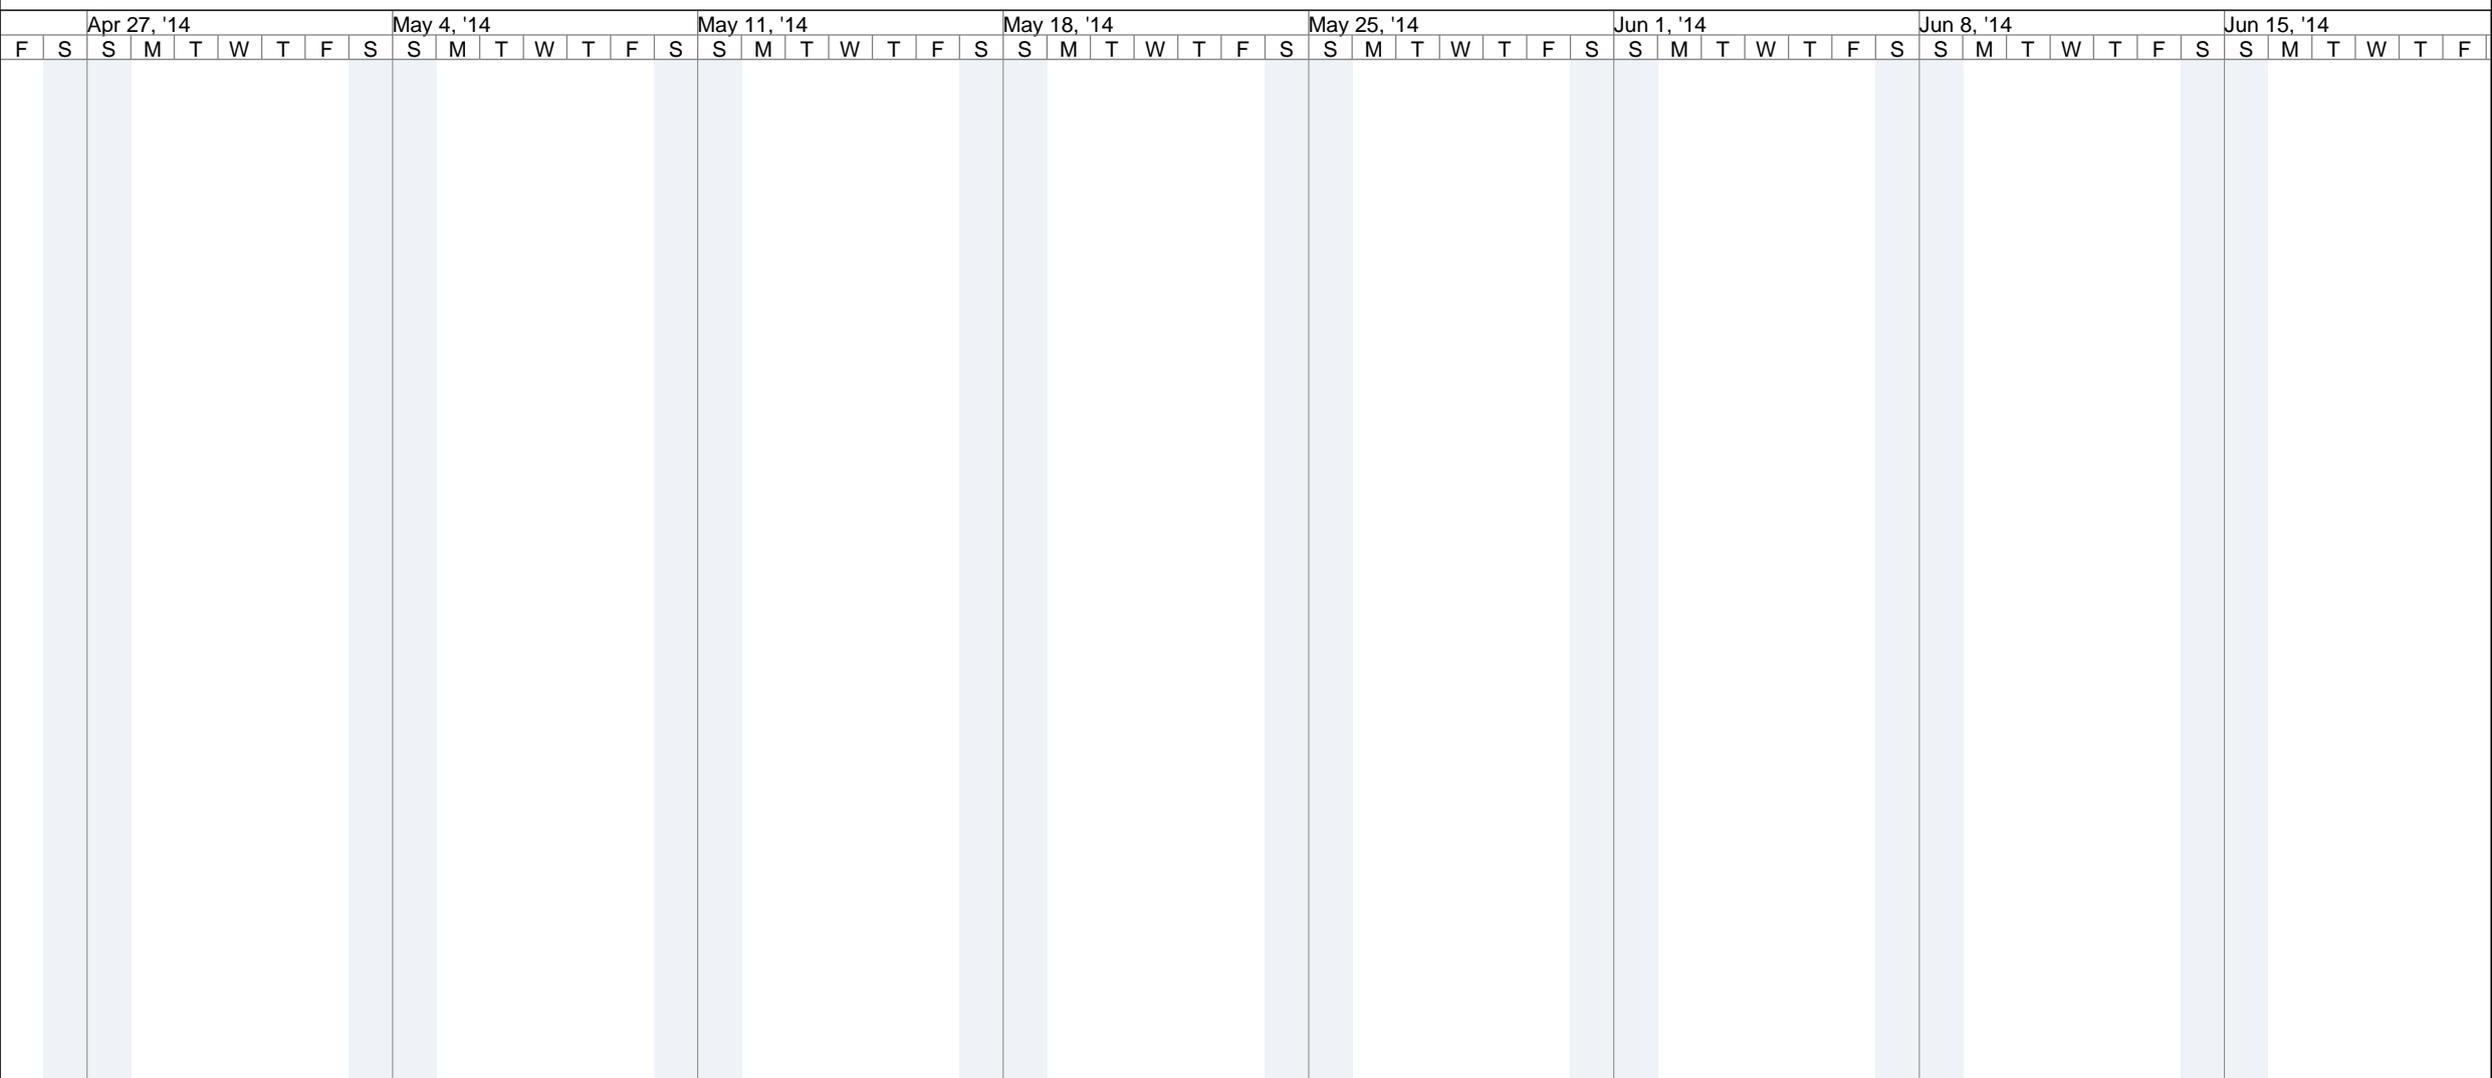


Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

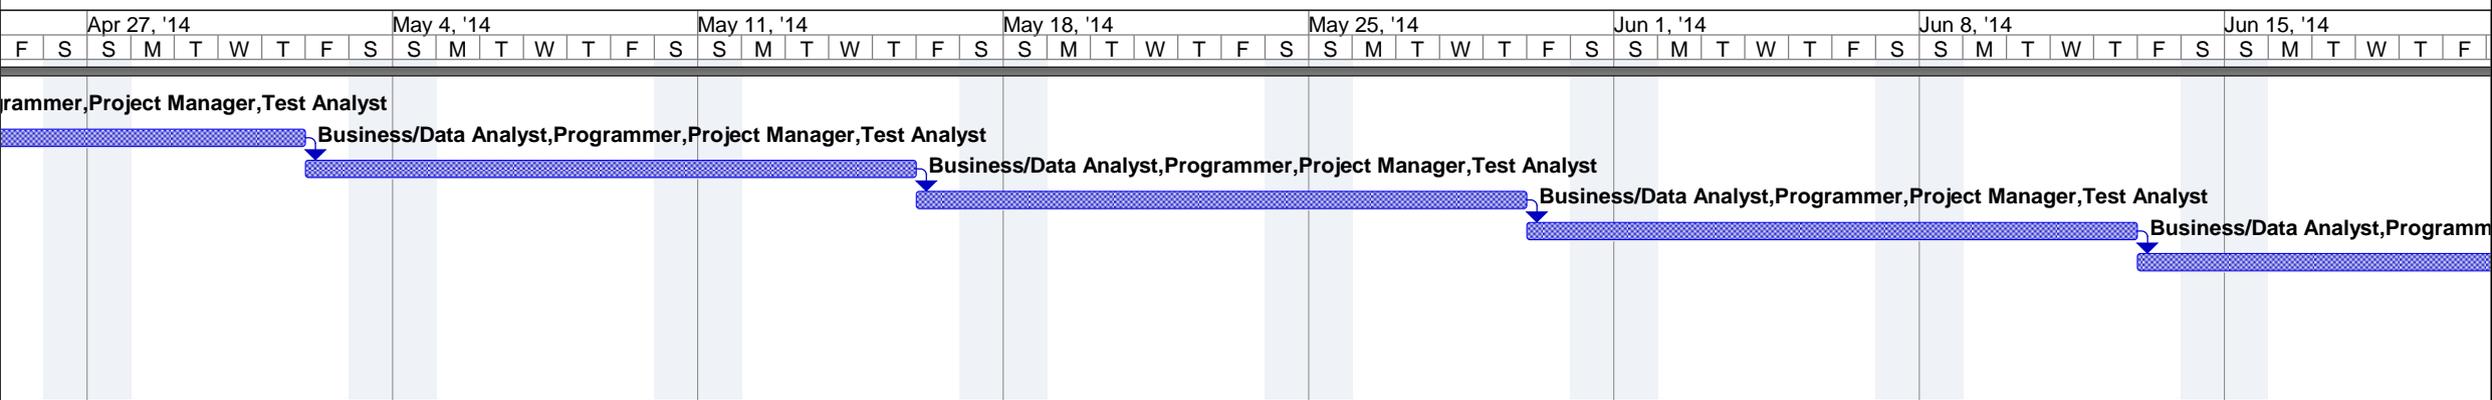


Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

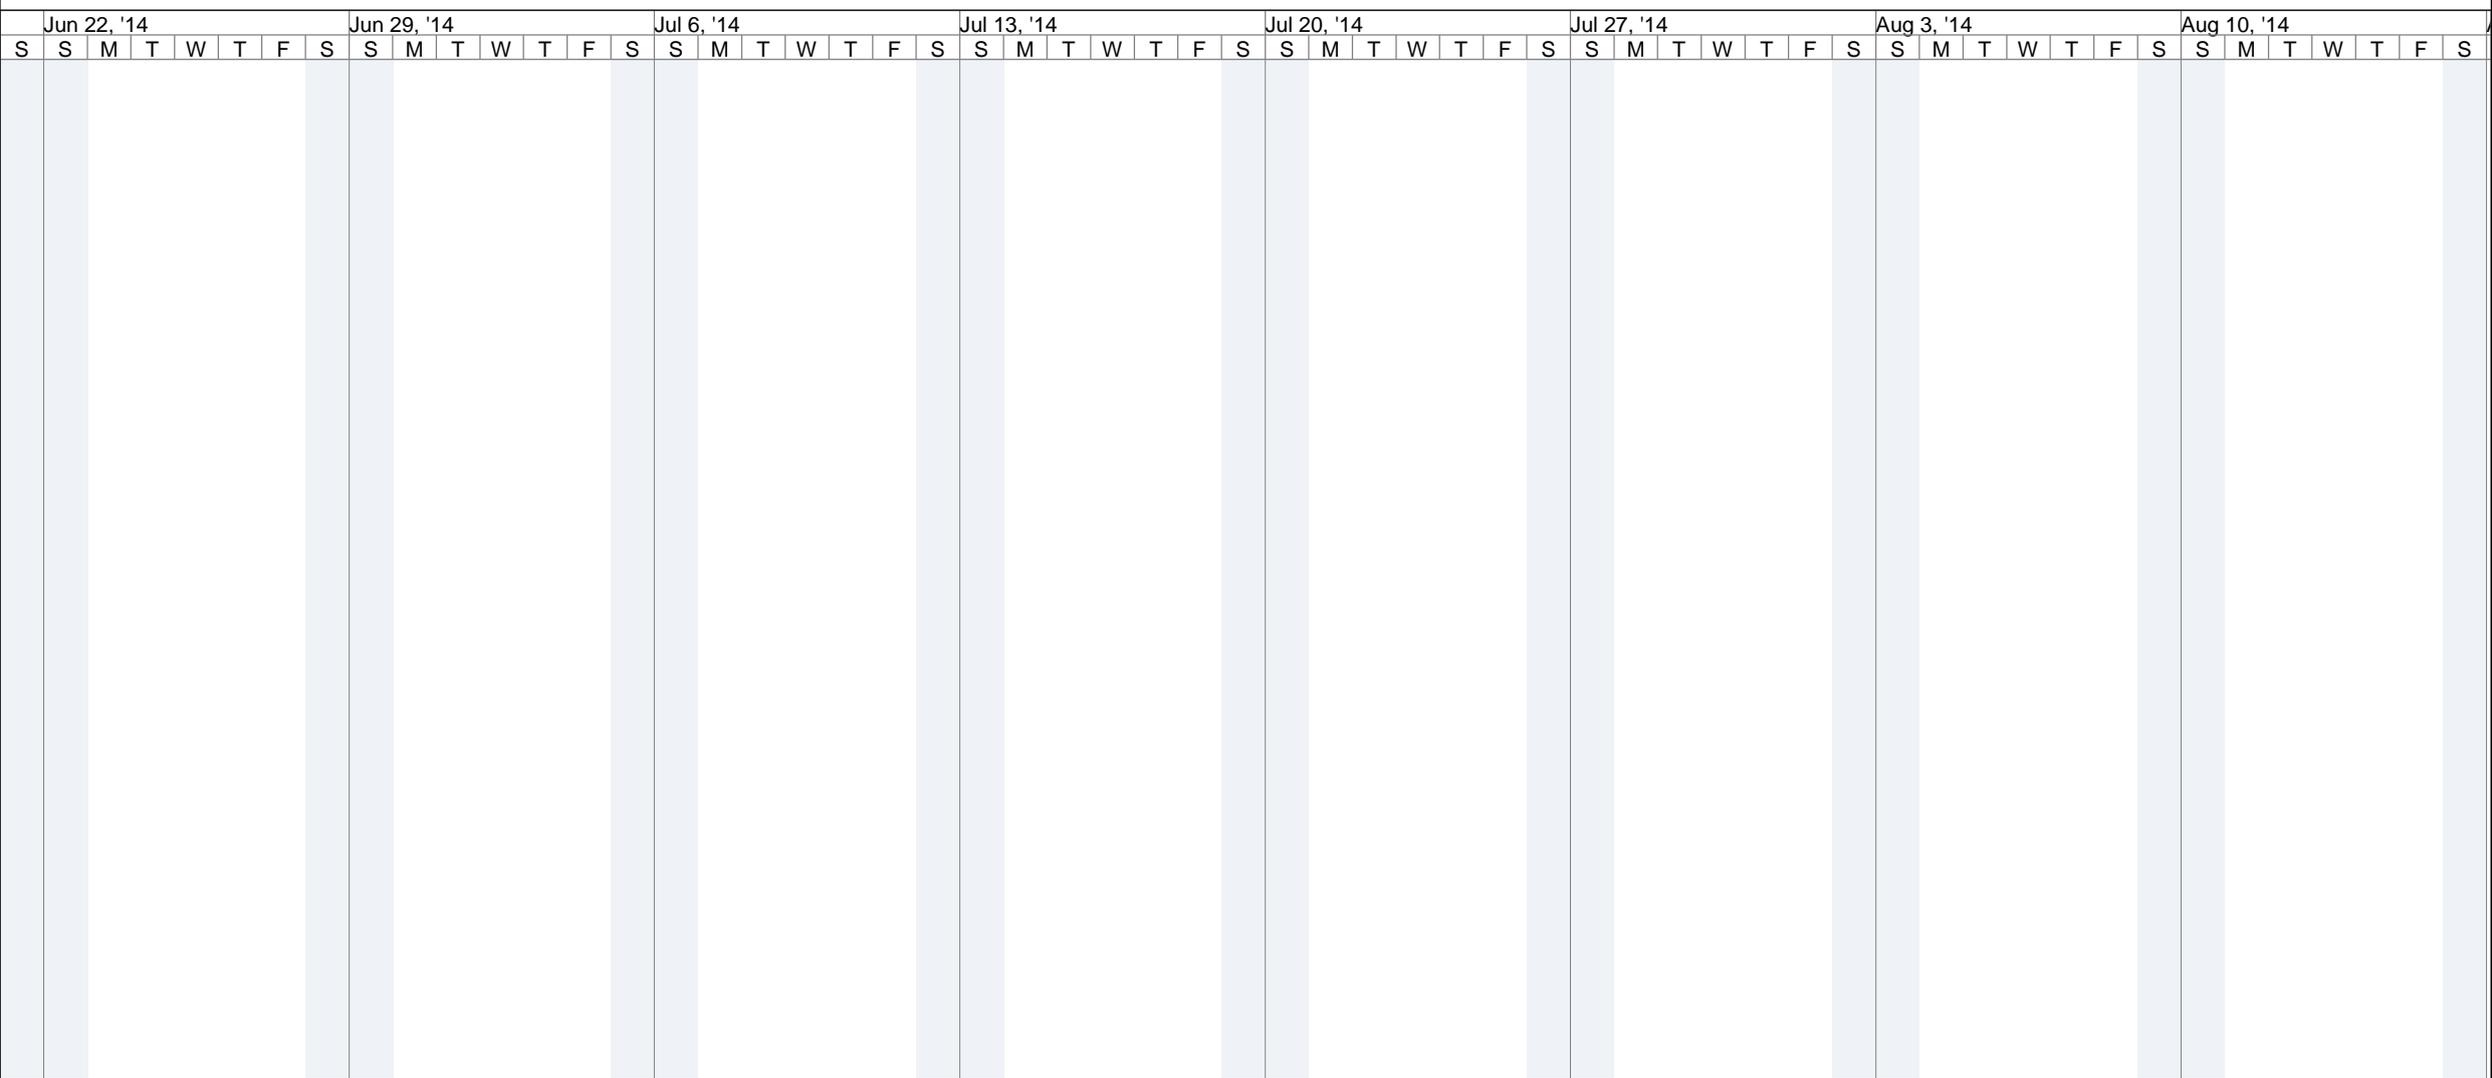

Project: Person Data Exchange Project  
 Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			

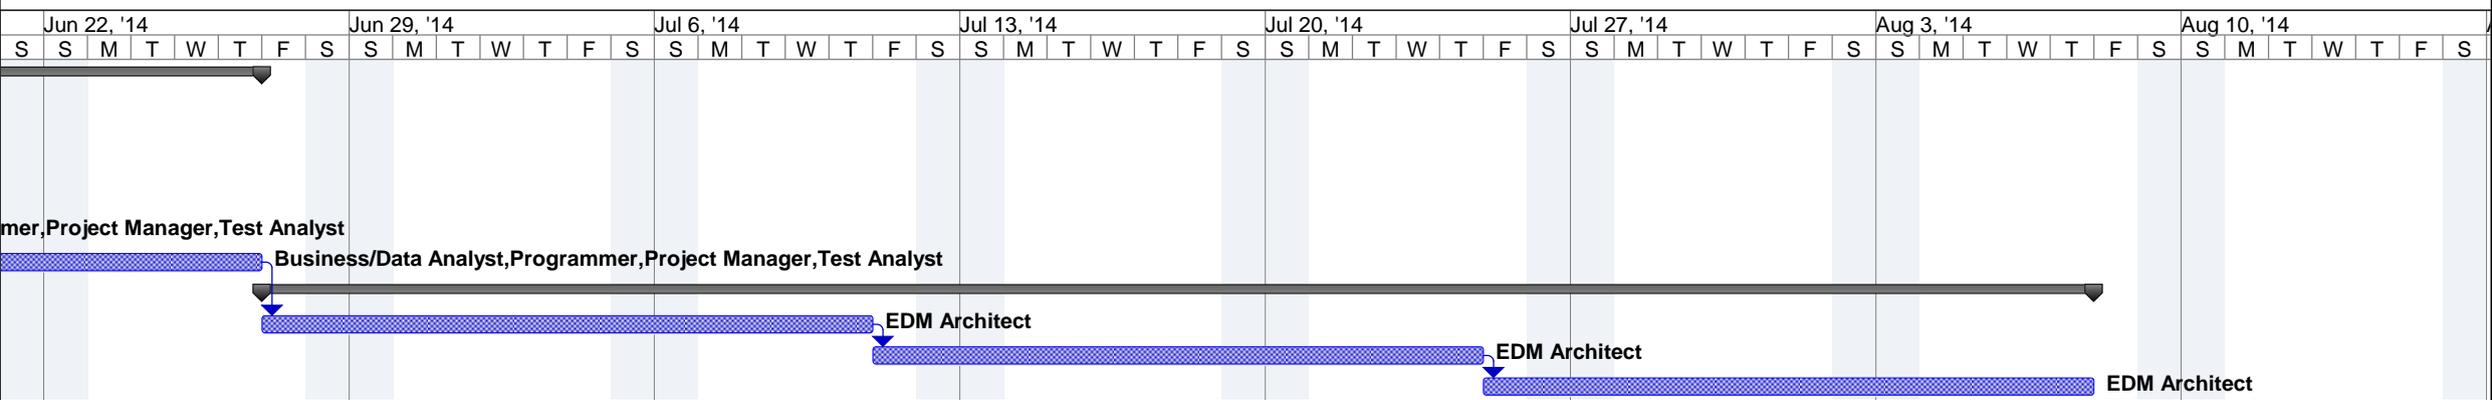

Project: Person Data Exchange Project  
Date: Tue 7/7/15

Task		External Tasks		Manual Task		Finish-only	
Split		External MileTask		Duration-only		Progress	
Milestone		Inactive Task		Manual Summary Rollup		Split	
Summary		Inactive Milestone		Manual Summary			
Project Summary		Inactive Summary		Start-only			
